



NORTH GENERAL AVIATION APRON RECONSTRUCTION

PROJECT

The project intends to remove the North GA Apron 1940's concrete and reconstruct with aggregate base course, underdrains, storm drain piping, trench drains, catch basins & manholes, asphalt surface course and pavement markings.



CONTRACTOR

Nelson Construction Corporation

ENGINEER OF RECORD

Mead & Hunt Engineering

PROJECT COST

Project Budget

\$7,222,359

Funding Sources

FAA Discretionary Grant

\$6,013,047

Airport Contribution

\$316,481

Port Contribution

\$892,731

SCHEDULE


W.A. #2: Behind in paving. Expected completion pushed back to Friday, Aug. 21.

W.A. #3: Expected start pushed back to Monday, Aug. 24.

**BE VIGILANT, WATCH FOR A/C,
PERSONS AND CONSTRUCTION
TRUCKS!**

[Work Area 5 Plan Sheet](#) (click to enlarge)

Proposed Work Schedule: 8/21/2026 – 9/22/2026

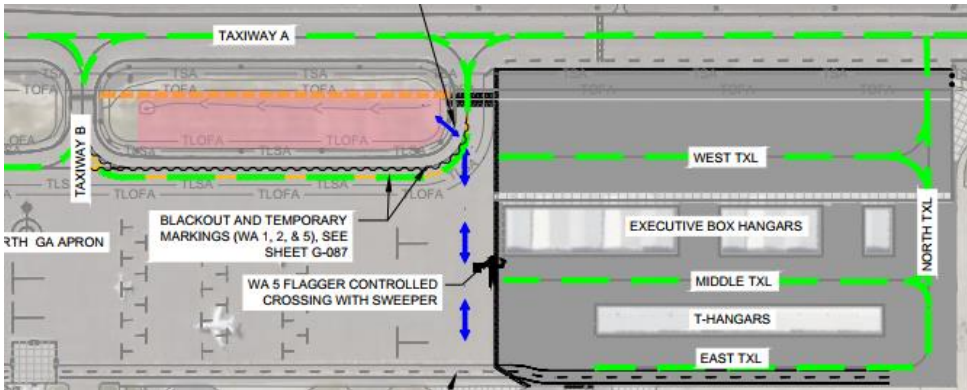

Allowed Work Hours

Monday-Friday: 6 AM - 6 PM


Impacts

*Will be constructed concurrently with other Work Areas.

BE VIGILANT, WATCH FOR A/C, PERSONS AND CONSTRUCTION TRUCKS!

[Work Area 3 Plan Sheet](#) (click to enlarge)

Contractor's Updated Work Schedule: 8/24/2026 – 10/12/2026

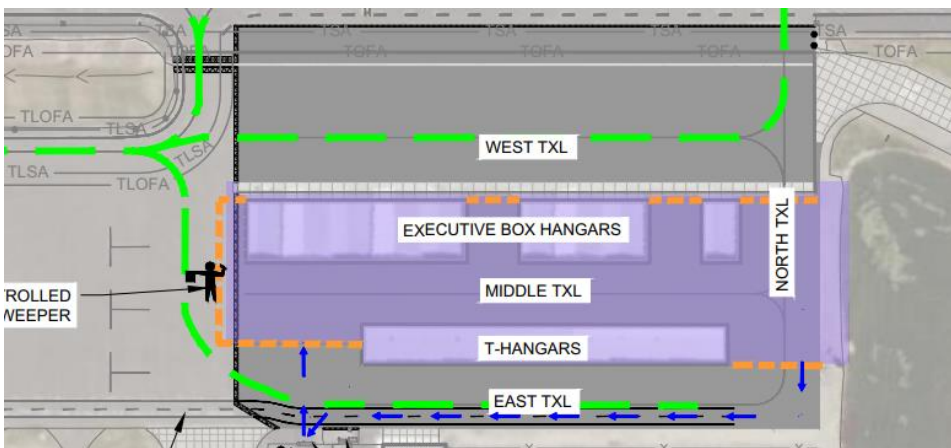

Allowed Work Hours

Monday-Friday: 6 AM - 6 PM


Impacts

*No Access to East-side Shelter hangars
*No Access to West-side T Hangars

BE VIGILANT, WATCH FOR A/C, PERSONS AND CONSTRUCTION TRUCKS!

[Work Area 4 Plan Sheet](#) (click to enlarge)

Proposed Work Schedule: 10/6/2026 – 10/30/2026

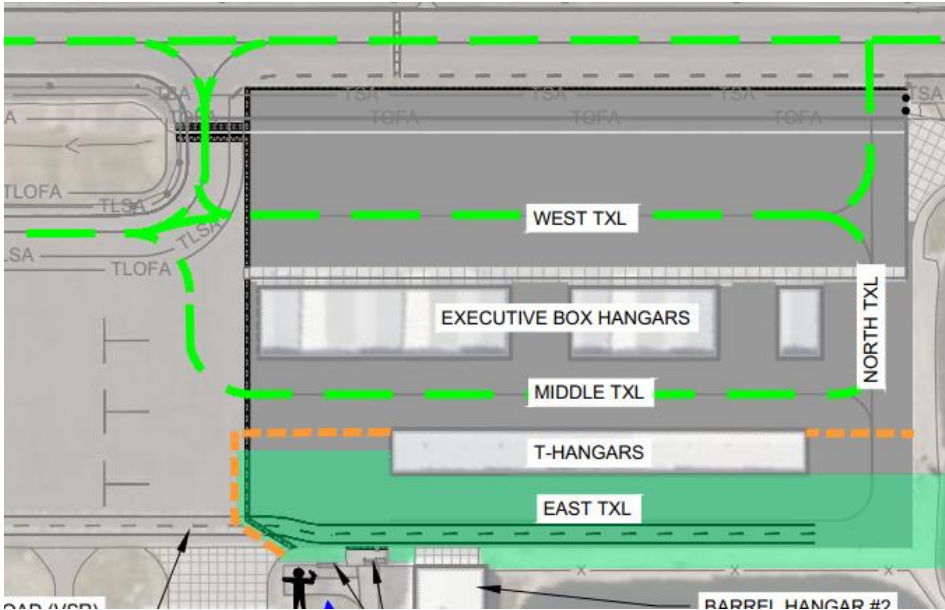

Allowed Work Hours

Monday-Friday: 6 AM - 6 PM

Impacts

- *No Access to East-side T Hangars
- *No Access to West-side Hangar

BE VIGILANT, WATCH FOR A/C,
PERSONS AND CONSTRUCTION
TRUCKS!

CONSTRUCTION SEASON ENDS OCTOBER 31, 2026

CURRENT CONTRACTOR SCHEDULE DEPICTS COMPLETION IN 2026
